Relay — Sprint 1 Dependency Map

Kopano Freight · AI-Powered Business Operations Platform · Sprint 1 (19–30 Oct 2026) · status as at Tue 20 Oct

How to read this

Every Sprint 1 story is listed with the stories it depends on. There are two kinds of dependency:

Can't start until	A **hard** dependency. You can't begin your story until the other story is merged to `main`. In the diagram it's a **solid arrow**.
Can start early with	A **soft** dependency. You can begin now using a stand-in (for example the classify stub), and connect the real thing when it lands. In the diagram it's a **dashed grey arrow**.
Unblocks	The stories that are waiting on yours. If you're late, these people are stuck, so say so at stand-up the same day.

Colour key (used in the diagram and tables)


Samukelo	Elzel	Mihlali	Baphakamise	All members

Three things that matter most

- **S1-01 (database) and S1-09 (sign-in) unblock the most work.** S1-01 is already done. S1-09 on Fri 23 Oct unblocks four stories across three people (S1-15, S1-18, S1-19, S1-22), so it's the riskiest date in the sprint.
- **Elzel's chain is the longest:** S1-02 → S1-06 → S1-10 → S1-16 → S1-21 → S1-25, one step every working day. Any slip pushes the real classifier past Tue 27 Oct. Mihlali and Baphakamise are protected because they build on the classify stub until then.
- **The plan has no clashes:** every story is scheduled after the stories it can't start without. The two same-day links (S1-26 and S1-28 on Wed 28) are tested together by Mihlali and Baphakamise.

Dependency diagram

Read left to right, one column per day. Arrows point from the story you need to the story that needs it. A thicker border means the story is done.

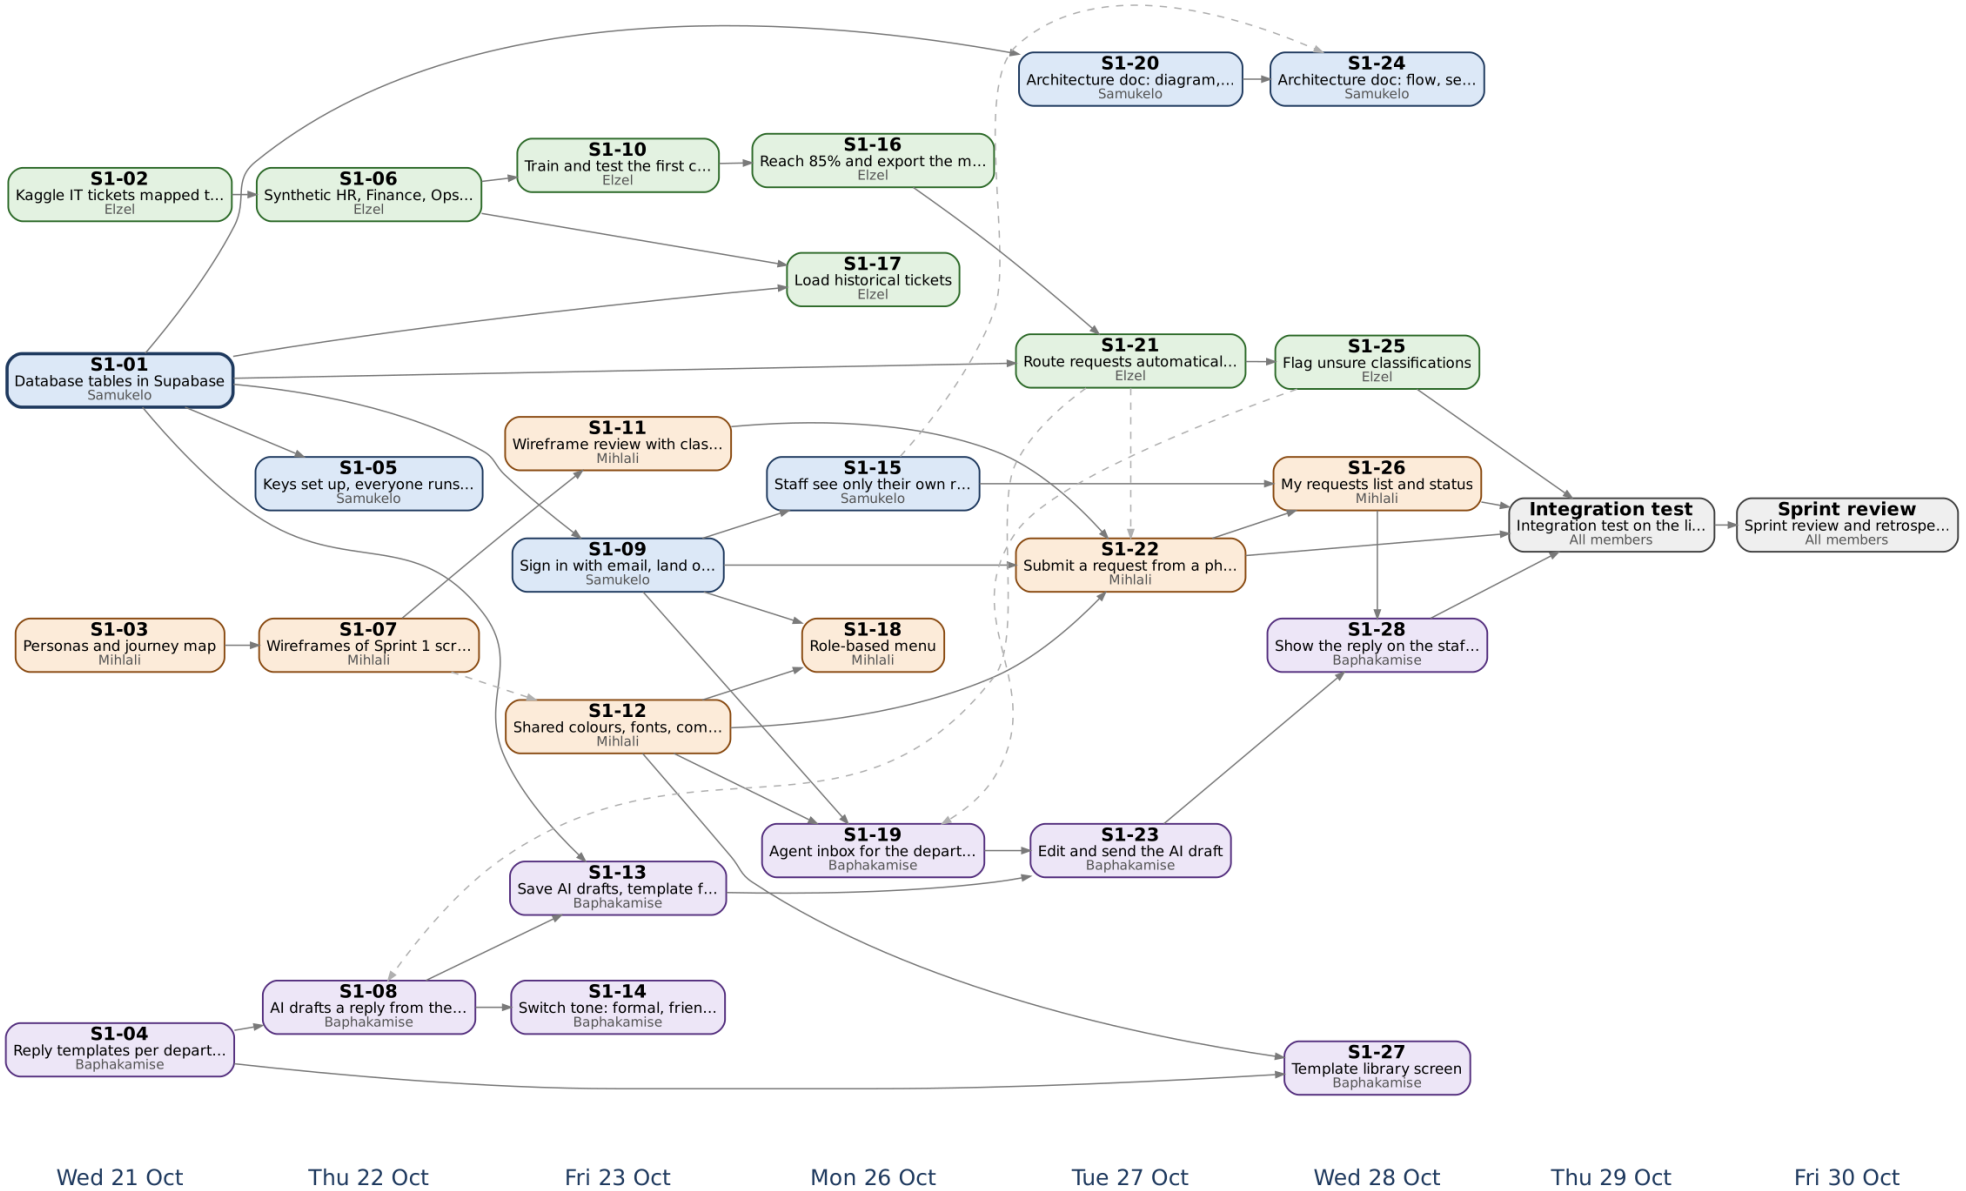

Story by story

Date	Story and owner	Can't start until	Can start early with	Unblocks
Wed 21	**S1-01** (Samukelo) **[Done]** Database tables in Supabase	**Nothing — start any time**	—	**S1-05** (Samukelo), **S1-09** (Samukelo), **S1-13** (Baphakamise), **S1-17** (Elzel), **S1-20** (Samukelo), **S1-21** (Elzel)
	S1-02 (Elzel) Kaggle IT tickets mapped to 4 departments	**Nothing — start any time**	—	**S1-06** (Elzel)
	S1-03 (Mihlali) Personas and journey map	**Nothing — start any time**	—	**S1-07** (Mihlali)
	S1-04 (Baphakamise) Reply templates per department	**Nothing — start any time**	—	**S1-08** (Baphakamise), **S1-27** (Baphakamise)
Thu 22	**S1-05** (Samukelo) **[In progress]** Keys set up, everyone runs the app locally	**S1-01** (Samukelo): Database tables in Supabase	—	—
	S1-06 (Elzel) Synthetic HR, Finance, Ops tickets	**S1-02** (Elzel): Kaggle IT tickets mapped to 4 departments	—	**S1-10** (Elzel), **S1-17** (Elzel)
	S1-07 (Mihlali) Wireframes of Sprint 1 screens	**S1-03** (Mihlali): Personas and journey map	—	**S1-11** (Mihlali)
	S1-08 (Baphakamise) AI drafts a reply from the template	**S1-04** (Baphakamise): Reply templates per department	**S1-21** (Elzel): use the classify stub already in the repo	**S1-13** (Baphakamise), **S1-14** (Baphakamise)
Fri 23	**S1-09** (Samukelo) Sign in with email, land on role home	**S1-01** (Samukelo): Database tables in Supabase	—	**S1-15** (Samukelo), **S1-18** (Mihlali), **S1-19** (Baphakamise), **S1-22** (Mihlali)
	S1-10 (Elzel) Train and test the first classifier	**S1-06** (Elzel): Synthetic HR, Finance, Ops tickets	—	**S1-16** (Elzel)
	S1-11 (Mihlali) Wireframe review with classmates	**S1-07** (Mihlali): Wireframes of Sprint 1 screens	—	**S1-22** (Mihlali)
	S1-12 (Mihlali) Shared colours, fonts, components	**Nothing — start any time**	**S1-07** (Mihlali): start with the default shadcn/ui look; adjust after wireframes	**S1-18** (Mihlali), **S1-19** (Baphakamise), **S1-22** (Mihlali), **S1-27** (Baphakamise)
	S1-13 (Baphakamise) Save AI drafts, template fallback	**S1-08** (Baphakamise): AI drafts a reply from the template **S1-01** (Samukelo): Database tables in Supabase	—	**S1-23** (Baphakamise)
	S1-14 (Baphakamise) Switch tone: formal, friendly, urgent	**S1-08** (Baphakamise): AI drafts a reply from the template	—	—
Mon 26	**S1-15** (Samukelo) Staff see only their own requests	**S1-09** (Samukelo): Sign in with email, land on role home	—	**S1-26** (Mihlali)

Date	Story and owner	Can't start until	Can start early with	Unblocks
	S1-16 (Elzel) Reach 85% and export the model	**S1-10** (Elzel): Train and test the first classifier	—	**S1-21** (Elzel)
	S1-17 (Elzel) Load historical tickets	**S1-01** (Samukelo): Database tables in Supabase **S1-06** (Elzel): Synthetic HR, Finance, Ops tickets	—	—
	S1-18 (Mihlali) Role-based menu	**S1-09** (Samukelo): Sign in with email, land on role home **S1-12** (Mihlali): Shared colours, fonts, components	—	—
	S1-19 (Baphakamise) Agent inbox for the department	**S1-09** (Samukelo): Sign in with email, land on role home **S1-12** (Mihlali): Shared colours, fonts, components	**S1-25** (Elzel): show the 'Needs review' marker from the needs_review column; it lights up once flagging is live	**S1-23** (Baphakamise)
Tue 27	**S1-20** (Samukelo) Architecture doc: diagram, components, data	**S1-01** (Samukelo): Database tables in Supabase	—	**S1-24** (Samukelo)
	S1-21 (Elzel) Route requests automatically (real model)	**S1-16** (Elzel): Reach 85% and export the model **S1-01** (Samukelo): Database tables in Supabase	—	**S1-25** (Elzel)
	S1-22 (Mihlali) Submit a request from a phone	**S1-09** (Samukelo): Sign in with email, land on role home **S1-11** (Mihlali): Wireframe review with classmates **S1-12** (Mihlali): Shared colours, fonts, components	**S1-21** (Elzel): call the classify stub; same input and output as the real model	**S1-26** (Mihlali), **Integration test**
	S1-23 (Baphakamise) Edit and send the AI draft	**S1-19** (Baphakamise): Agent inbox for the department **S1-13** (Baphakamise): Save AI drafts, template fallback	—	**S1-28** (Baphakamise)
Wed 28	**S1-24** (Samukelo) Architecture doc: flow, security, plans	**S1-20** (Samukelo): Architecture doc: diagram, components, data	**S1-15** (Samukelo): describe the planned role rules if S1-15 slips	—
	S1-25 (Elzel) Flag unsure classifications	**S1-21** (Elzel): Route requests automatically (real model)	—	**Integration test**
	S1-26 (Mihlali) My requests list and status	**S1-22** (Mihlali): Submit a request from a phone **S1-15** (Samukelo): Staff see only their own requests	—	**S1-28** (Baphakamise), **Integration test**

Date	Story and owner	Can't start until	Can start early with	Unblocks
	S1-27 (Baphakamise) Template library screen	**S1-04** (Baphakamise): Reply templates per department **S1-12** (Mihlali): Shared colours, fonts, components	—	—
	S1-28 (Baphakamise) Show the reply on the staff request	**S1-23** (Baphakamise): Edit and send the AI draft **S1-26** (Mihlali): My requests list and status	—	**Integration test**
Thu 29	**Integration test** Integration test on the live site	**S1-22** (Mihlali): Submit a request from a phone **S1-25** (Elzel): Flag unsure classifications **S1-26** (Mihlali): My requests list and status **S1-28** (Baphakamise): Show the reply on the staff request	—	**Sprint review**
Fri 30	**Sprint review** Sprint review and retrospective	**Integration test**: Integration test on the live site	—	—

Who waits for whom

For each person: whose work you need before you can start, and who is waiting on you.

Member	You wait for (from someone else)	Others wait for you
Samukelo	Nobody — your stories only depend on your own work	Your **S1-01** → **S1-13** (Baphakamise) Your **S1-01** → **S1-21** (Elzel) Your **S1-01** → **S1-17** (Elzel) Your **S1-09** → **S1-18** (Mihlali) Your **S1-09** → **S1-22** (Mihlali) Your **S1-09** → **S1-19** (Baphakamise) Your **S1-15** → **S1-26** (Mihlali)
Elzel	**S1-01** (Samukelo) before your **S1-17** (Mon 26) **S1-01** (Samukelo) before your **S1-21** (Tue 27)	Your **S1-25** → **Integration test**
Mihlali	**S1-09** (Samukelo) before your **S1-18** (Mon 26) **S1-09** (Samukelo) before your **S1-22** (Tue 27) **S1-15** (Samukelo) before your **S1-26** (Wed 28)	Your **S1-12** → **S1-19** (Baphakamise) Your **S1-12** → **S1-27** (Baphakamise) Your **S1-22** → **Integration test** Your **S1-26** → **Integration test** Your **S1-26** → **S1-28** (Baphakamise)
Baphakamise	**S1-01** (Samukelo) before your **S1-13** (Fri 23) **S1-09** (Samukelo) before your **S1-19** (Mon 26) **S1-12** (Mihlali) before your **S1-19** (Mon 26) **S1-12** (Mihlali) before your **S1-27** (Wed 28) **S1-26** (Mihlali) before your **S1-28** (Wed 28)	Your **S1-28** → **Integration test**

If you're blocked

- Say so at stand-up **the same day**, naming the story you're waiting on.
- Check the **Can start early with** column: most UI work can begin against the classify stub or sample data.
- Meanwhile, pick up a story of yours with **Nothing — start any time**, or help the person you're waiting on.
